

# The Right Life

Neo build ventures



## Monthly Photographs

# KEY PLAN




Lake-side lifestyle

Large event lawn area

Water zone with kid's pool and boardwalk pool

# THE RIGHT LIFE PROJECT

## Phase 1.1 – Key Plan

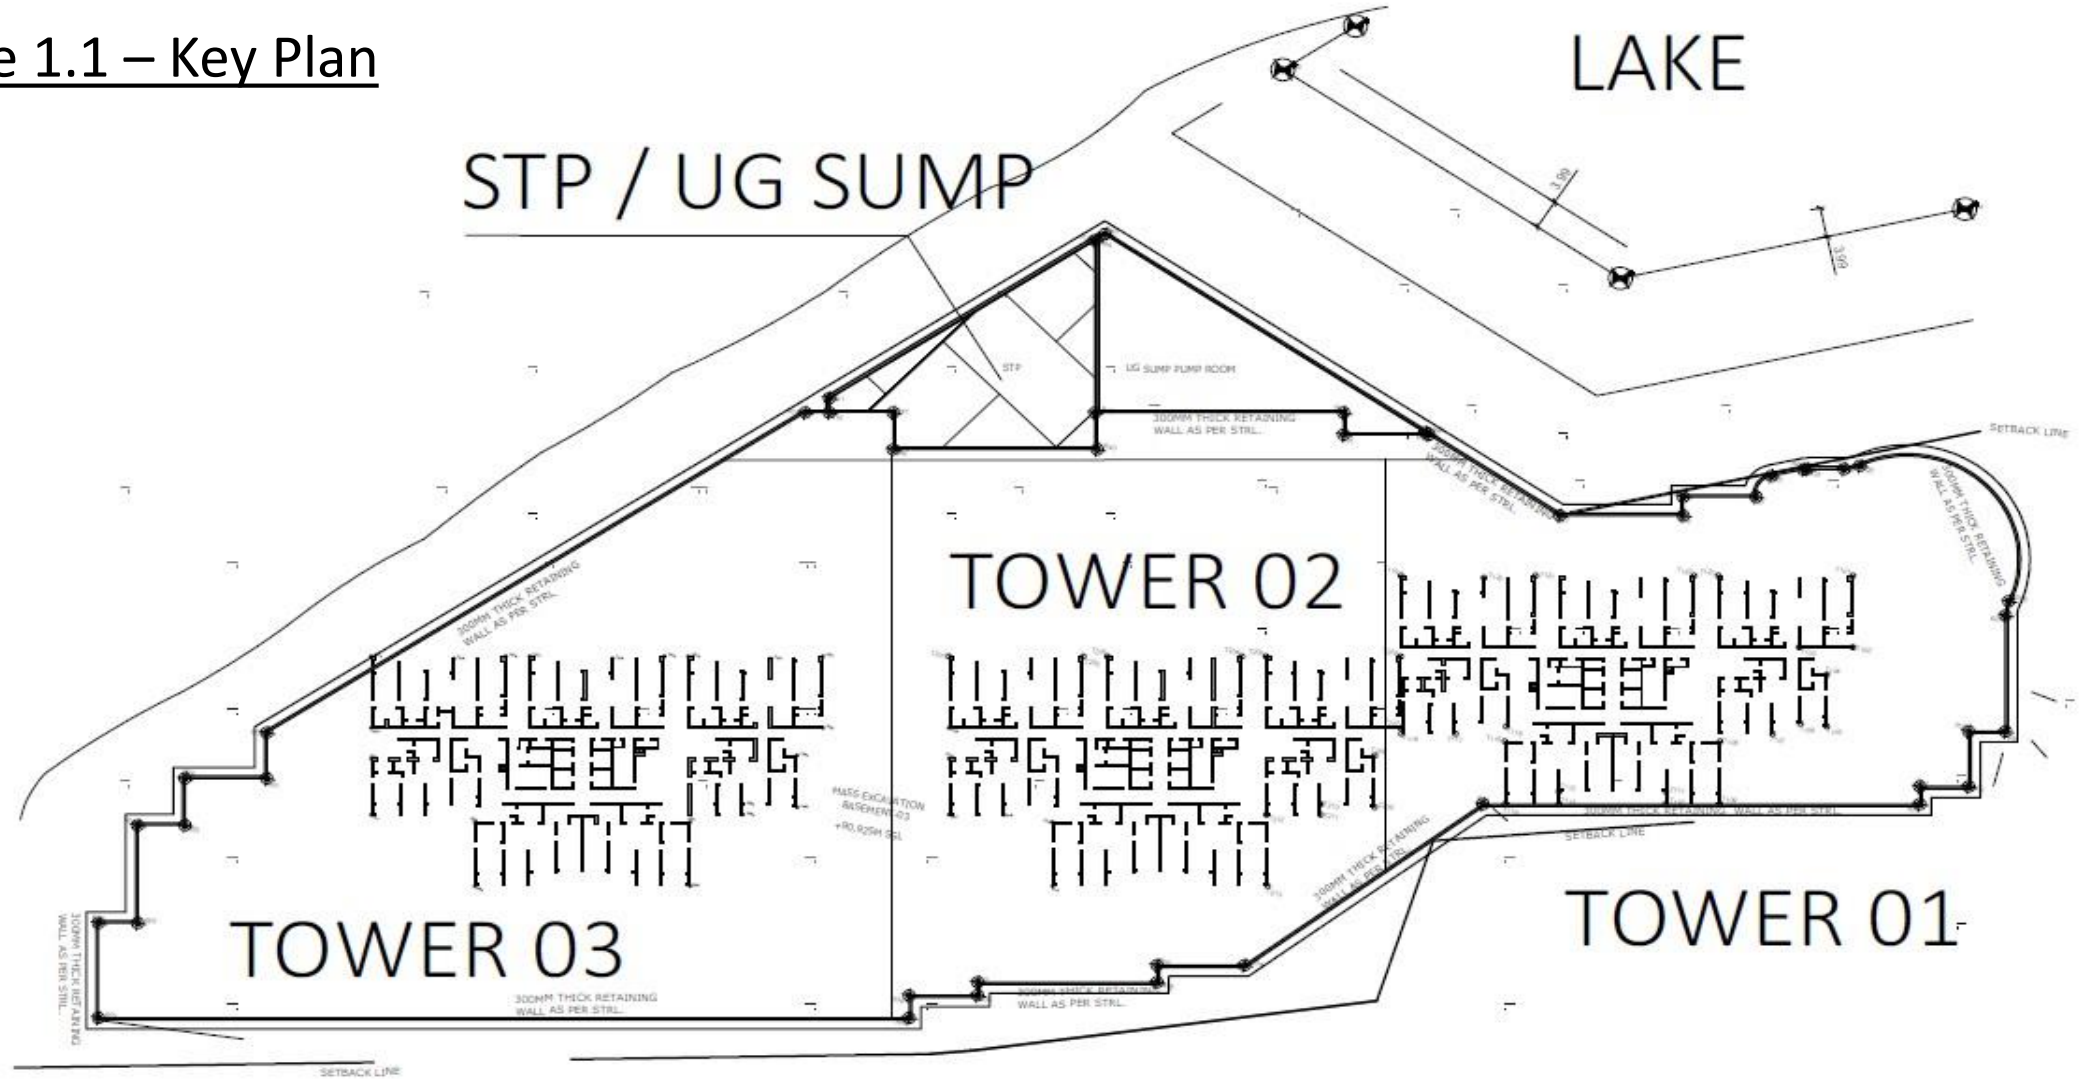

# THE RIGHT LIFE PROJECT

Phase 1.1 – Tower 01



Tower 1	Raft	Shear wall	Slab
B 01		46%	
B 02		100%	50%
B 03	100%	100%	100%

# THE RIGHT LIFE PROJECT

Phase 1.1 – Tower 02



Tower 2	Raft	Shear wall	Slab
B 01		76%	
B 02		100%	42%
B 03	100%	100%	85%

# THE RIGHT LIFE PROJECT


Phase 1.1 – Tower 03



Tower 3	Raft	Shear wall	Slab
B 01			
B 02			
B 03	37%		

# THE RIGHT LIFE PROJECT

Phase 1.2 – Tower 07 - 09

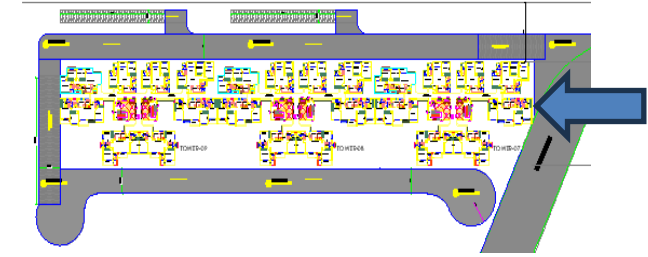

- Excavation 88% completed

# THE RIGHT LIFE PROJECT

## Achieved in the month of March

- Tower 01
  - Basement 02 Roof Slab Pour 03 – Concrete - Completed
  - Basement 02 Roof Slab Pour 04 – Shuttering - 70%
  - Basement 01 Roof Slab Pour 01 – Shuttering - 70%
  
- Tower 02
  - Basement 03 Roof Slab Pour 05 – Concrete - Completed
  - Basement 02 Roof Slab Pour 03 – Concrete - Completed
  - Basement 02 Roof Slab Pour 03A – Concrete - Completed
  
- Tower 03
  - Raft PCC Works - 100%
  - Stitch slab - 50%
  - Pedestal - 38%

# THE RIGHT LIFE PROJECT

## Target for the month of April

- Tower 01
  - Basement 02 Roof Slab Concrete - 80%
  - Basement 01 Roof Slab Concrete - 25%
  
- Tower 02
  - Basement 03 Roof Slab Concrete - 80%
  - Basement 02 Roof Slab Concrete - 80%
  - Basement 01 Roof Slab Concrete - 25%
  
- Tower 03
  - Raft PCC Works - 100%
  - Stitch slab - 75%
  - Pedestal - 75%
