



<b>Project:</b> Medway Municipal Complex Project	<b>Monthly Report No.:</b> 8
<b>Job No:</b> n/a	<b>Month of:</b> March 2026
<b>Architect:</b> Dore + Whittier Architects 260 Merrimac Street, 2 <sup>nd</sup> Floor Newburyport, MA 01950	<b>Owner:</b> Town of Medway 155 Village Street Medway, MA 02053

<b>Director:</b> Phil Palumbo	<b>Email:</b> phil.palumbo@collierseng.com
<b>Project Manager:</b> Luis Rodriguez	<b>Email:</b> luis.rodriguez@collierseng.com

**Project Progress During/Through Month of March:**

3/5	Schedule Meeting and Budget Subcommittee Mtg
3/13	Site Design Progress Meeting
3/13	Intro. Meeting with Cyber Comm.
3/16	DRC Meeting
3/23	Pull Planning Session for Design & GMP Schedule
3/23	Building Committee Meeting
3/1 - 3/31	Schematic Design Progresses
3/1 - 3/31	Cost Estimate Coordination
3/1 - 3/31	Traffic Study Finalization
3/1 - 3/31	Invoice Processing & Budget Updating
3/1 - 3/31	Design Schedule Analyzing

**30 Day Look Ahead Summary (March):**

4/6/26	SD Set to Estimator
4/6 - 4/20	SD Design Review
4/13/26	Building Committee Meeting to Review SD Review
4/27/26	SD Estimates due from estimator
4/29/26	SD Estimate Reconciliation Meeting


**Potential Issues:**

	1st noted (period ending)	Status
1) None at this time.		


**Attachments**

- Project Schedule dated 4/14/2026


# PROGRESS

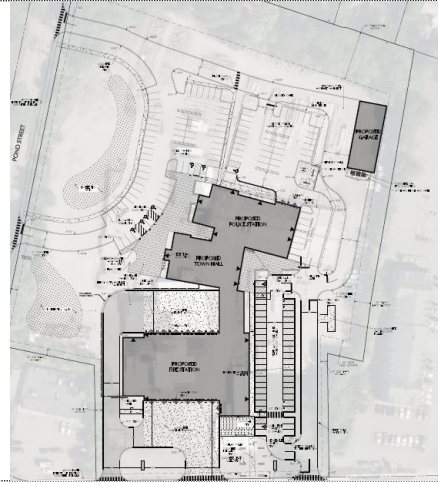


Site Plan – SD Progress Drawings

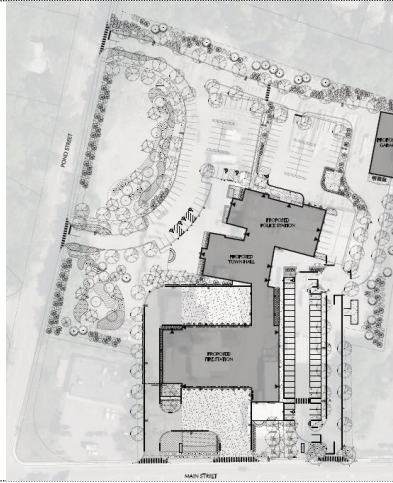

Planting Plan – SD Progress Drawings

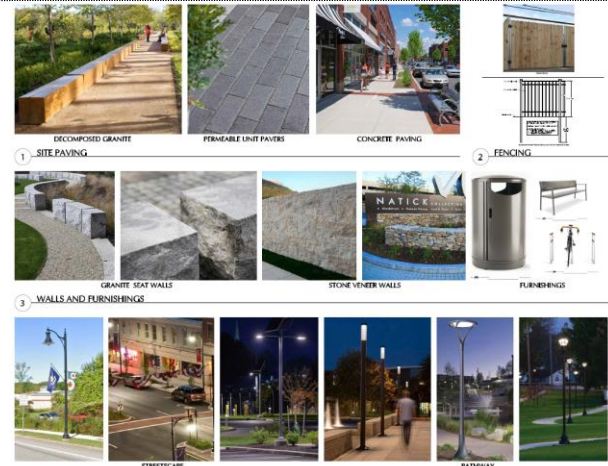


Precedent Imagery -

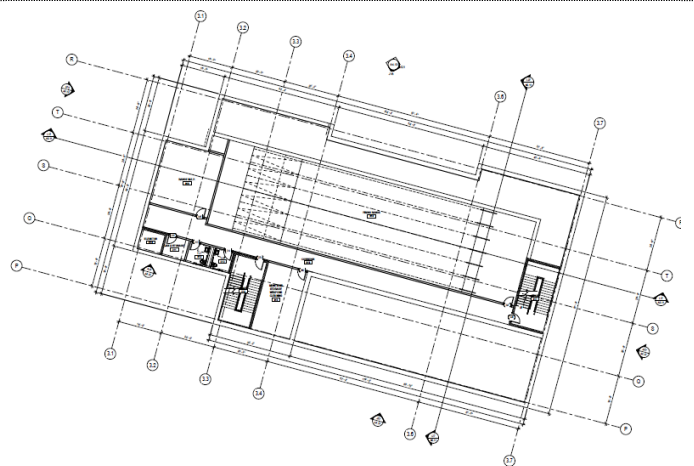

Basement Plan - SD Progress Drawings



First Plan - SD Progress Drawings

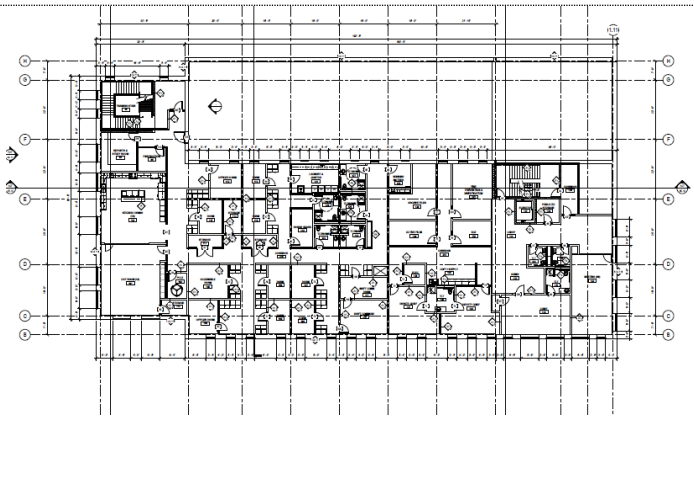

Second Plan - SD Progress Drawings

End of Report

