



Project: Medway Municipal Complex Project	Monthly Report No.: 12
Job No: n/a	Month of: July 2026
Architect: Dore + Whittier Architects 260 Merrimac Street, 2nd Floor Newburyport, MA 01950	Owner: Town of Medway 155 Village Street Medway, MA 02053

Director: Phil Palumbo	Email: phil.palumbo@collierseng.com
Project Manager: Luis Rodriguez	Email: luis.rodriguez@collierseng.com

Project Progress During/Through Month of July:

7/1	Door Hardware + Access Control Meeting - Town Hall
7/7	Interdepartmental Review Meeting
7/8	Mass Save Charette Meeting
7/22	DD Estimate Reconciliation Meeting
7/27	Building Committee Meeting
7/30	Security + Station Alerting Meeting
7/1 – 7/31	Weekly Team Check-In Meetings

30 Day Look Ahead Summary (July):

8/3	DRC Meeting
8/6	Equipment + Maintenance Needs
8/11	Planning Board Meeting
8/24	Building Committee Meeting
8/1 – 8/31	Weekly Team Check-Ins

Potential Issues:


	1st noted (period ending)	Status
1) None at this time.		

Attachments

- Project Schedule dated 8/3/2026

PROGRESS

**Berm Plans
& Sections**

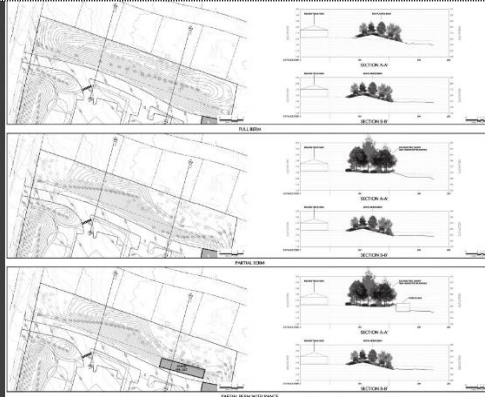

**Color Site
Plan**



Looking South



Looking Southeast



Looking East



Looking Northeast



Looking North



Town of Medway

Medway Municipal Complex Project
