



**Weekly Construction Project Report No. 030**

# Lake Shamineau High Water Outlet Project

**PREPARED FOR:** Lake Shamineau Lake Improvement District  
**PREPARED BY:** Beau Sanford  
**DATE:** April 28, 2024  
**HEI PROJECT NO.:** 9276-0003

## Reporting Period

April 22, 2024 - April 26, 2024

## Project Details

**Project Name:** Lake Shamineau High Water Outlet  
**Current Project Value Completed:** \$3,887,773.28 (Through Application for Payment #6)  
**Contractor:** Landwehr Construction Inc.

## Weather Summary This Week:

**M** - clear sky 30s Deg., High 60s Deg., Wind 10 MPH.  
**T** - light intensity drizzle 30s Deg., High 50s Deg., Wind 12 MPH.

## Summary of Work Performed by Contractor

- Ward Custom Homes was onsite to install the service door and finish installing the metal siding on the outside of the pump house.

## Future Activities

- Look ahead schedule unavailable, only cleanup work and minor pump station work to be completed in the next week.
- Landwehr is awaiting bituminous plants in the area to open. It is anticipated that these plants will be opening in May.

\*All information for this report was collected from the Houston Resident Project Representative’s Logs.



Photo #1: Installing the service door for the pump house - Apr 22, 2024, 10:02 AM

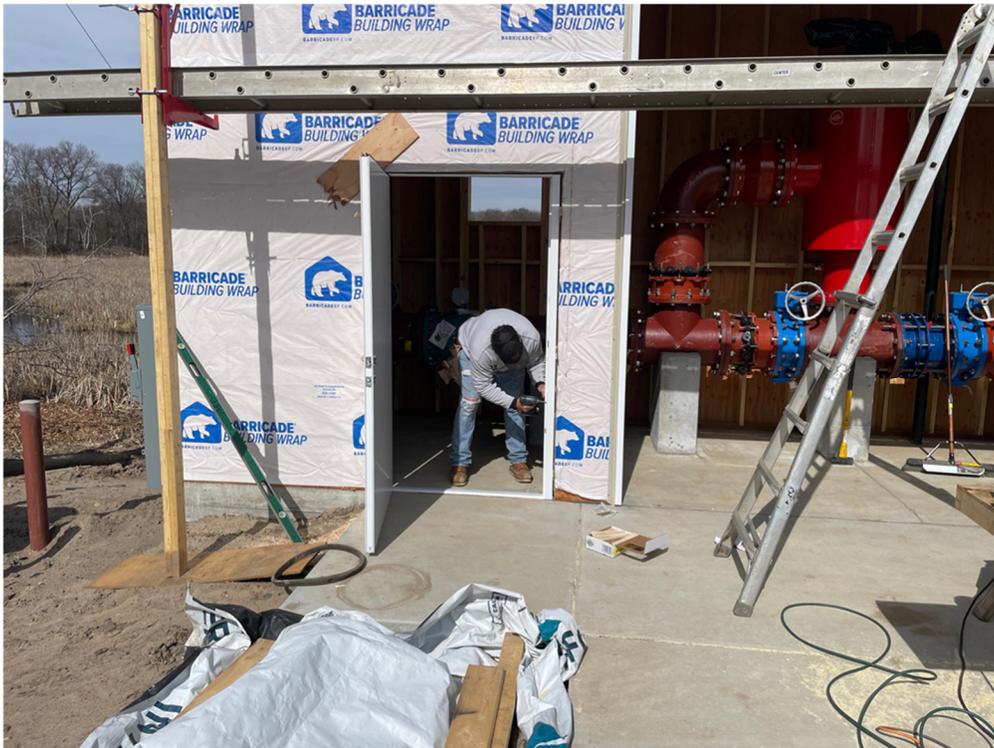


Photo #2: Attaching the door frame to the building framework - Apr 22, 2024, 10:27 AM



Photo #3: Nailing metal edging to the pump house around the service door - Apr 22, 2024, 1:02 PM



Photo #4: Continuing to nail on metal siding - Apr 23, 2024, 9:15 AM



Photo #5: Installing the steel corners on the pump house exterior - Apr 23, 2024, 12:37 PM



Photo #6: View of pump house from Aztec Road - Apr 23, 2024, 1:15 PM
