

Project: Tolt Schedule Utility Re
Date: Fri 11/4/22

| | | | | | | | | | |
|-----------|--|--------------------|--|-----------------------|--|--------------------|--|-----------------|--|
| Task | | Project Summary | | Manual Task | | Start-only | | Deadline | |
| Split | | Inactive Task | | Duration-only | | Finish-only | | Progress | |
| Milestone | | Inactive Milestone | | Manual Summary Rollup | | External Tasks | | Manual Progress | |
| Summary | | Inactive Summary | | Manual Summary | | External Milestone | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Qtr 2, 2022 | | | Qtr 3, 2022 | | | Qtr 4, 2022 | | | Qtr 1, 2023 | | | Qtr 2, 2023 | | | Qtr 3, 2023 | |
|----|-----------|-------------------------------------|----------------|--------------------|--------------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|--|
| | | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | |
| 38 | → | CB2 - CB3 28'-30" | 1 day | Mon 7/11/22 | Mon 7/11/22 | | | | | | | | | | | | | | | | | |
| 39 | → | CB3 - CB4 52'-30" | 1 day | Tue 7/12/22 | Tue 7/12/22 | | | | | | | | | | | | | | | | | |
| 40 | → | CB4 - CB6 126'-30" | 1 day | Wed 7/13/22 | Wed 7/13/22 | | | | | | | | | | | | | | | | | |
| 41 | → | CB6 - CB9 32'-24" | 1 day | Thu 7/14/22 | Thu 7/14/22 | | | | | | | | | | | | | | | | | |
| 42 | → | SEWER | 26 days | Fri 7/15/22 | Sat 8/13/22 | | | | | | | | | | | | | | | | | |
| 43 | → | SEWER VALVE PITS | 12 days | Fri 7/15/22 | Thu 7/28/22 | | | | | | | | | | | | | | | | | |
| 44 | → | ROAD A | 3 days | Fri 7/15/22 | Mon 7/18/22 | | | | | | | | | | | | | | | | | |
| 45 | → | SSVP w/SS #1-5 | 3 days | Fri 7/15/22 | Mon 7/18/22 | | | | | | | | | | | | | | | | | |
| 46 | → | ROAD B | 5 days | Tue 7/19/22 | Sat 7/23/22 | | | | | | | | | | | | | | | | | |
| 47 | → | SSVP w/SS 58,57 | 1 day | Tue 7/19/22 | Tue 7/19/22 | | | | | | | | | | | | | | | | | |
| 48 | → | SSVP w/SS 53,55 | 1 day | Wed 7/20/22 | Wed 7/20/22 | | | | | | | | | | | | | | | | | |
| 49 | → | SSVP w/SS 57,56 | 1 day | Thu 7/21/22 | Thu 7/21/22 | | | | | | | | | | | | | | | | | |
| 50 | → | SSVP w/SS 52,51 | 1 day | Fri 7/22/22 | Fri 7/22/22 | | | | | | | | | | | | | | | | | |
| 51 | → | SSVP w/SS 50,49 | 1 day | Sat 7/23/22 | Sat 7/23/22 | | | | | | | | | | | | | | | | | |
| 52 | → | ROAD C | 4 days | Mon 7/25/22 | Thu 7/28/22 | | | | | | | | | | | | | | | | | |
| 53 | → | SSVP w/SS 24,25 | 1 day | Mon 7/25/22 | Mon 7/25/22 | | | | | | | | | | | | | | | | | |
| 54 | → | SSVP w/SS 26,27 | 1 day | Tue 7/26/22 | Tue 7/26/22 | | | | | | | | | | | | | | | | | |
| 55 | → | SSVP w/SS 28,29 | 1 day | Wed 7/27/22 | Wed 7/27/22 | | | | | | | | | | | | | | | | | |
| 56 | → | SSVP w/SS 30 | 1 day | Thu 7/28/22 | Thu 7/28/22 | | | | | | | | | | | | | | | | | |
| 57 | → | SEWER MAIN | 10 days | Fri 7/29/22 | Tue 8/9/22 | | | | | | | | | | | | | | | | | |
| 58 | → | SEWER MAIN 48+00 TO 12+00 (1900 LF) | 1 day | Fri 7/29/22 | Fri 7/29/22 | | | | | | | | | | | | | | | | | |
| 59 | → | TESTING DELAY | 3 days | Sat 7/30/22 | Tue 8/2/22 | | | | | | | | | | | | | | | | | |
| 60 | → | SEWER MAIN 48+00 TO 12+00 | 4 days | Fri 8/5/22 | Tue 8/9/22 | | | | | | | | | | | | | | | | | |
| 61 | → | SEWER VALVE PITS | 1 day | Sat 8/13/22 | Sat 8/13/22 | | | | | | | | | | | | | | | | | |
| 62 | → | ROAD A | 1 day | Sat 8/13/22 | Sat 8/13/22 | | | | | | | | | | | | | | | | | |
| 63 | → | SSVP w/SS 6,7 | 1 day | Sat 8/13/22 | Sat 8/13/22 | | | | | | | | | | | | | | | | | |
| 64 | → | STORM | 37 days | Mon 8/15/22 | Tue 9/27/22 | | | | | | | | | | | | | | | | | |
| 65 | → | POND - CB 40, 41, 42, 43 | 1 day | Mon 8/15/22 | Mon 8/15/22 | | | | | | | | | | | | | | | | | |
| 66 | → | CB43 - CB44, 42 TO 95, 95 TO 45 | 1 day | Tue 8/16/22 | Tue 8/16/22 | | | | | | | | | | | | | | | | | |
| 67 | → | CB45 - CB93 57'-12" | 1 day | Wed 8/17/22 | Wed 8/17/22 | | | | | | | | | | | | | | | | | |
| 68 | → | CB45 - CB94, POND CB 29, TO CB 30 | 1 day | Thu 8/18/22 | Thu 8/18/22 | | | | | | | | | | | | | | | | | |
| 69 | → | CB30 - CB31, CB 31 TO CB 35 | 1 day | Fri 8/19/22 | Fri 8/19/22 | | | | | | | | | | | | | | | | | |
| 70 | → | CB30 - CB46 104'-12" | 1 day | Sat 8/20/22 | Sat 8/20/22 | | | | | | | | | | | | | | | | | |
| 71 | → | CB46 - CB47 142'-12" | 1 day | Tue 9/27/22 | Tue 9/27/22 | | | | | | | | | | | | | | | | | |
| 72 | → | CB 4 TO CB 5 TO CB 92 | 2 days | Sat 9/24/22 | Mon 9/26/22 | | | | | | | | | | | | | | | | | |
| 73 | → | SEWER | 18 days | Mon 8/22/22 | Mon 9/12/22 | | | | | | | | | | | | | | | | | |
| 74 | → | ROAD D SEWER | 18 days | Mon 8/22/22 | Mon 9/12/22 | | | | | | | | | | | | | | | | | |

Project: Tolt Schedule Utility Re
Date: Fri 11/4/22

| | | | | | | | | | |
|-----------|--|--------------------|--|-----------------------|--|--------------------|--|-----------------|--|
| Task | | Project Summary | | Manual Task | | Start-only | | Deadline | |
| Split | | Inactive Task | | Duration-only | | Finish-only | | Progress | |
| Milestone | | Inactive Milestone | | Manual Summary Rollup | | External Tasks | | Manual Progress | |
| Summary | | Inactive Summary | | Manual Summary | | External Milestone | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Qtr 2, 2022 | | | Qtr 3, 2022 | | | Qtr 4, 2022 | | | Qtr 1, 2023 | | | Qtr 2, 2023 | | | Qtr 3, 2023 | | |
|-----|-----------|--|----------------|---------------------|---------------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|--|--|
| | | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | | |
| 75 | → | SSVP w/SS 67,66 | 1 day | Mon 8/22/22 | Mon 8/22/22 | | | | | | | | | | | | | | | | | | |
| 76 | → | SSVP w/SS 65,64 | 1 day | Tue 8/23/22 | Tue 8/23/22 | | | | | | | | | | | | | | | | | | |
| 77 | → | SSVP w/SS 63,62 | 1 day | Wed 8/24/22 | Wed 8/24/22 | | | | | | | | | | | | | | | | | | |
| 78 | → | SSVP w/SS 61,60 | 1 day | Thu 8/25/22 | Thu 8/25/22 | | | | | | | | | | | | | | | | | | |
| 79 | → | SSVP w/SS 59 | 1 day | Fri 8/26/22 | Fri 8/26/22 | | | | | | | | | | | | | | | | | | |
| 80 | → | Over Ex topsoil Pile | 4 days | Sat 8/27/22 | Wed 8/31/22 | | | | | | | | | | | | | | | | | | |
| 81 | → | SSVP w/SS 11,12 | 1 day | Thu 9/1/22 | Thu 9/1/22 | | | | | | | | | | | | | | | | | | |
| 82 | → | SSVP w/SS 13,14 | 1 day | Fri 9/2/22 | Fri 9/2/22 | | | | | | | | | | | | | | | | | | |
| 83 | → | 8" SEWER MAIN SSB 28 TO SSCO #3 (700 LF) | 3 days | Sat 9/3/22 | Wed 9/7/22 | | | | | | | | | | | | | | | | | | |
| 84 | → | 8" SEWER MAIN SSB 30 TO SSCO #4 (325 LF) | 1 day | Thu 9/8/22 | Thu 9/8/22 | | | | | | | | | | | | | | | | | | |
| 85 | → | SSVP w/SS 10,9 | 1 day | Fri 9/9/22 | Fri 9/9/22 | | | | | | | | | | | | | | | | | | |
| 86 | → | SSVP w/SS 8,74 | 1 day | Sat 9/10/22 | Sat 9/10/22 | | | | | | | | | | | | | | | | | | |
| 87 | → | SSVP w/SS 75,76 | 1 day | Mon 9/12/22 | Mon 9/12/22 | | | | | | | | | | | | | | | | | | |
| 88 | → | WATER | 17 days | Tue 9/13/22 | Sat 10/1/22 | | | | | | | | | | | | | | | | | | |
| 89 | → | ROAD A | 10 days | Tue 9/13/22 | Fri 9/23/22 | | | | | | | | | | | | | | | | | | |
| 90 | → | Water Main sta. 10+64 to 19+00 | 6 days | Tue 9/13/22 | Mon 9/19/22 | | | | | | | | | | | | | | | | | | |
| 91 | → | Water Services st. 10+64 to 19+00 | 4 days | Tue 9/20/22 | Fri 9/23/22 | | | | | | | | | | | | | | | | | | |
| 92 | → | ROAD B | 4 days | Wed 9/28/22 | Sat 10/1/22 | | | | | | | | | | | | | | | | | | |
| 93 | → | Water Main sta. 34+00 to 30+00 | 2 days | Wed 9/28/22 | Thu 9/29/22 | | | | | | | | | | | | | | | | | | |
| 94 | → | Water Services st. 34+00 to 30+00 | 2 days | Fri 9/30/22 | Sat 10/1/22 | | | | | | | | | | | | | | | | | | |
| 95 | → | STORM | 2 days | Mon 10/3/22 | Tue 10/4/22 | | | | | | | | | | | | | | | | | | |
| 96 | → | CB28 - CB29, CB 31 TO CB 32 | 1 day | Mon 10/3/22 | Mon 10/3/22 | | | | | | | | | | | | | | | | | | |
| 97 | → | CB32 - CB33, CB 34 TO CB 35 | 1 day | Tue 10/4/22 | Tue 10/4/22 | | | | | | | | | | | | | | | | | | |
| 98 | → | WATER | 10 days | Wed 10/5/22 | Sat 10/15/22 | | | | | | | | | | | | | | | | | | |
| 99 | → | ROAD D | 10 days | Wed 10/5/22 | Sat 10/15/22 | | | | | | | | | | | | | | | | | | |
| 100 | → | Water Main sta. 60+00 to 64+50 | 4 days | Wed 10/5/22 | Sat 10/8/22 | | | | | | | | | | | | | | | | | | |
| 101 | → | Water Services st. 60+00 to 64+50 | 3 days | Thu 10/13/22 | Sat 10/15/22 | | | | | | | | | | | | | | | | | | |
| 102 | → | SEWER | 29 days | Mon 10/10/22 | Sat 11/12/22 | | | | | | | | | | | | | | | | | | |
| 103 | → | Fire Station Sewer Revision | 3 days | Mon 10/10/22 | Wed 10/12/22 | | | | | | | | | | | | | | | | | | |
| 104 | → | Revised Fire Station Sewer RFI | 2 days | Fri 11/11/22 | Sat 11/12/22 | | | | | | | | | | | | | | | | | | |
| 105 | → | WATER | 55 days | Tue 10/18/22 | Sat 12/24/22 | | | | | | | | | | | | | | | | | | |
| 106 | → | ROAD C | 55 days | Tue 10/18/22 | Sat 12/24/22 | | | | | | | | | | | | | | | | | | |
| 107 | → | Water Main sta. 45+00 to 48+00 | 3 days | Tue 10/18/22 | Thu 10/20/22 | | | | | | | | | | | | | | | | | | |
| 108 | → | Water Main sta. 43+20 to 48+00 | 3 days | Fri 10/21/22 | Mon 10/24/22 | | | | | | | | | | | | | | | | | | |
| 109 | → | WATER SERVICES | 3 days | Tue 10/25/22 | Thu 10/27/22 | | | | | | | | | | | | | | | | | | |
| 110 | → | Watermain C-900 to DI RFI | 9 days | Thu 12/15/22 | Sat 12/24/22 | | | | | | | | | | | | | | | | | | |

| | | | | | | | | | | |
|--|-----------|--|--------------------|--|-----------------------|--|--------------------|--|-----------------|--|
| Project: Tolt Schedule Utility Re Date: Fri 11/4/22 | Task | | Project Summary | | Manual Task | | Start-only | | Deadline | |
| | Split | | Inactive Task | | Duration-only | | Finish-only | | Progress | |
| | Milestone | | Inactive Milestone | | Manual Summary Rollup | | External Tasks | | Manual Progress | |
| | Summary | | Inactive Summary | | Manual Summary | | External Milestone | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Qtr 2, 2022 | | | Qtr 3, 2022 | | | Qtr 4, 2022 | | | Qtr 1, 2023 | | | Qtr 2, 2023 | | | Qtr 3, 2023 | | |
|-----|-----------|--|-----------------|---------------------|---------------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|--|--|
| | | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | | |
| 111 | ➔ | SEWER | 3 days | Wed 8/10/22 | Fri 8/12/22 | | | | | | | | | | | | | | | | | | |
| 112 | ➔ | School Sewer Tie-In SSB43 - SSB38 234'-8" | 3 days | Wed 8/10/22 | Fri 8/12/22 | | | | | | | | | | | | | | | | | | |
| 113 | ➔ | WATER FRONTAGE | 9 days | Mon 12/5/22 | Wed 12/14/22 | | | | | | | | | | | | | | | | | | |
| 114 | ➔ | H2O BORING PER RFI TENATIVE DEC START PER SUB | 2 days | Mon 12/5/22 | Tue 12/6/22 | | | | | | | | | | | | | | | | | | |
| 115 | ➔ | SR203 Water Main sta. 103+17 to 108 | 7 days | Wed 12/7/22 | Wed 12/14/22 | | | | | | | | | | | | | | | | | | |
| 116 | ➔ | STORM FRONTAGE | 4 days | Mon 11/7/22 | Thu 11/10/22 | | | | | | | | | | | | | | | | | | |
| 117 | ➔ | WEATHER WINDOW WATER TABLE TO DROP | 0 days | Mon 11/7/22 | Mon 11/7/22 | | | | | | | | | | | | | | | | | | |
| 118 | ➔ | CB 90 - CB 84 | 4 days | Mon 11/7/22 | Thu 11/10/22 | | | | | | | | | | | | | | | | | | |
| 119 | ➔ | WATER | 5 days | Fri 10/28/22 | Wed 11/2/22 | | | | | | | | | | | | | | | | | | |
| 120 | ➔ | Deep Water Sections | 5 days | Fri 10/28/22 | Wed 11/2/22 | | | | | | | | | | | | | | | | | | |
| 121 | ➔ | Road A Water Main @ sta. 10+50 | 1 day | Fri 10/28/22 | Fri 10/28/22 | | | | | | | | | | | | | | | | | | |
| 122 | ➔ | Road A Water Main @ sta. 18+50 | 1 day | Sat 10/29/22 | Sat 10/29/22 | | | | | | | | | | | | | | | | | | |
| 123 | ➔ | Road D Water Main @ sta. 60+00 | 2 days | Mon 10/31/22 | Tue 11/1/22 | | | | | | | | | | | | | | | | | | |
| 124 | ➔ | Road D Water Main @ sta. 62+00 | 1 day | Wed 11/2/22 | Wed 11/2/22 | | | | | | | | | | | | | | | | | | |
| 125 | ➔ | STORM | 143 days | Tue 9/13/22 | Mon 3/6/23 | | | | | | | | | | | | | | | | | | |
| 126 | ➔ | ROAD C | 2 days | Tue 12/27/22 | Wed 12/28/22 | | | | | | | | | | | | | | | | | | |
| 127 | ➔ | CB74 - CB 96 | 2 days | Tue 12/27/22 | Wed 12/28/22 | | | | | | | | | | | | | | | | | | |
| 128 | ➔ | TRACT B | 1 day | Thu 12/29/22 | Thu 12/29/22 | | | | | | | | | | | | | | | | | | |
| 129 | ➔ | CB34 - CB 39 | 1 day | Thu 12/29/22 | Thu 12/29/22 | | | | | | | | | | | | | | | | | | |
| 130 | ➔ | ROAD C | 1 day | Fri 12/30/22 | Fri 12/30/22 | | | | | | | | | | | | | | | | | | |
| 131 | ➔ | CB35 - CB36 28'-12" | 1 day | Fri 12/30/22 | Fri 12/30/22 | | | | | | | | | | | | | | | | | | |
| 132 | ➔ | ROAD D | 4 days | Tue 9/13/22 | Fri 9/16/22 | | | | | | | | | | | | | | | | | | |
| 133 | ➔ | CB 9 - CB 11 | 1 day | Tue 9/13/22 | Tue 9/13/22 | | | | | | | | | | | | | | | | | | |
| 134 | ➔ | CB11 - CB13 130'-24" | 1 day | Wed 9/14/22 | Wed 9/14/22 | | | | | | | | | | | | | | | | | | |
| 135 | ➔ | CB13 - CB14, CB 14 TO 16 | 1 day | Thu 9/15/22 | Thu 9/15/22 | | | | | | | | | | | | | | | | | | |
| 136 | ➔ | CB16 - CB17, CB 17 TO CB 18, CB 14 TO CB 15, CB 13 TO CB 51, CB 9 TO | 1 day | Fri 9/16/22 | Fri 9/16/22 | | | | | | | | | | | | | | | | | | |
| 137 | ➔ | ROAD A | 1 day | Mon 10/17/22 | Mon 10/17/22 | | | | | | | | | | | | | | | | | | |
| 138 | ➔ | CB6 - CB8 | 1 day | Mon 10/17/22 | Mon 10/17/22 | | | | | | | | | | | | | | | | | | |
| 139 | ➔ | TRACT F | 1 day | Sat 9/17/22 | Sat 9/17/22 | | | | | | | | | | | | | | | | | | |
| 140 | ➔ | CB11 - CB27 | 1 day | Sat 9/17/22 | Sat 9/17/22 | | | | | | | | | | | | | | | | | | |
| 141 | ➔ | LOT DRAINS | 8 days | Sat 2/25/23 | Mon 3/6/23 | | | | | | | | | | | | | | | | | | |
| 142 | ➔ | LOTS 137-140, LOT 127-136, LOT 107-114 | 1 day | Sat 2/25/23 | Sat 2/25/23 | | | | | | | | | | | | | | | | | | |
| 143 | ➔ | LOTS 119-126, WALL 6 DRAIN | 1 day | Mon 2/27/23 | Mon 2/27/23 | | | | | | | | | | | | | | | | | | |

Project: Tolt Schedule Utility Re
Date: Fri 11/4/22

| | | | | | | | | | |
|-----------|--|--------------------|--|-----------------------|--|--------------------|--|-----------------|--|
| Task | | Project Summary | | Manual Task | | Start-only | | Deadline | |
| Split | | Inactive Task | | Duration-only | | Finish-only | | Progress | |
| Milestone | | Inactive Milestone | | Manual Summary Rollup | | External Tasks | | Manual Progress | |
| Summary | | Inactive Summary | | Manual Summary | | External Milestone | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Qtr 2, 2022 | | | Qtr 3, 2022 | | | Qtr 4, 2022 | | | Qtr 1, 2023 | | | Qtr 2, 2023 | | | Qtr 3, 2023 | |
|-----|-----------|---|----------------|---------------------|--------------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|--|
| | | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | |
| 144 | ➔ | LOTS 115-118, LOT 102-106, LOT 101-98, LOT 97-94, LOT 90-93 | 1 day | Tue 2/28/23 | Tue 2/28/23 | | | | | | | | | | | | | | | | | |
| 145 | ➔ | LOTS 85-89, LOT 50-51 | 1 day | Wed 3/1/23 | Wed 3/1/23 | | | | | | | | | | | | | | | | | |
| 146 | ➔ | LOTS 44-49 - 270' w/ 6 C/O | 1 day | Thu 3/2/23 | Thu 3/2/23 | | | | | | | | | | | | | | | | | |
| 147 | ➔ | LOTS 83-84, LOT 81-82, LOT 77-80 | 1 day | Fri 3/3/23 | Fri 3/3/23 | | | | | | | | | | | | | | | | | |
| 148 | ➔ | Wall 5 Drain, LOT 1-3 | 1 day | Sat 3/4/23 | Sat 3/4/23 | | | | | | | | | | | | | | | | | |
| 149 | ➔ | LOTS 3-6, WALL 1 DRAIN | 1 day | Mon 3/6/23 | Mon 3/6/23 | | | | | | | | | | | | | | | | | |
| 150 | ➔ | SEWER P2 | 20 days | Sat 12/31/22 | Wed 1/25/23 | | | | | | | | | | | | | | | | | |
| 151 | ➔ | SSVP w/ SS | 13 days | Sat 12/31/22 | Tue 1/17/23 | | | | | | | | | | | | | | | | | |
| 152 | ➔ | Sewer Main | 7 days | Wed 1/18/23 | Wed 1/25/23 | | | | | | | | | | | | | | | | | |
| 153 | ➔ | STORM P2 | 25 days | Thu 1/26/23 | Thu 2/23/23 | | | | | | | | | | | | | | | | | |
| 154 | ➔ | Road C Storm | 5 days | Thu 1/26/23 | Tue 1/31/23 | | | | | | | | | | | | | | | | | |
| 155 | ➔ | Road A Storm | 5 days | Wed 2/1/23 | Mon 2/6/23 | | | | | | | | | | | | | | | | | |
| 156 | ➔ | Road E Storm | 3 days | Tue 2/7/23 | Thu 2/9/23 | | | | | | | | | | | | | | | | | |
| 157 | ➔ | Lot & Wall Drains | 12 days | Fri 2/10/23 | Thu 2/23/23 | | | | | | | | | | | | | | | | | |
| 158 | ➔ | Water P2 | 13 days | Fri 2/10/23 | Fri 2/24/23 | | | | | | | | | | | | | | | | | |
| 159 | ➔ | Water Main | 9 days | Fri 2/10/23 | Mon 2/20/23 | | | | | | | | | | | | | | | | | |
| 160 | ➔ | Water Services | 4 days | Tue 2/21/23 | Fri 2/24/23 | | | | | | | | | | | | | | | | | |
| 161 | ➔ | Walls | 13 days | Wed 9/14/22 | Wed 9/28/22 | | | | | | | | | | | | | | | | | |
| 162 | ➔ | WALL 1 | 2 days | Wed 9/14/22 | Thu 9/15/22 | | | | | | | | | | | | | | | | | |
| 163 | ➔ | WALL 4 | 3 days | Fri 9/16/22 | Mon 9/19/22 | | | | | | | | | | | | | | | | | |
| 164 | ➔ | WALL 6 | 2 days | Tue 9/20/22 | Wed 9/21/22 | | | | | | | | | | | | | | | | | |
| 165 | ➔ | WALL 7 | 2 days | Thu 9/22/22 | Fri 9/23/22 | | | | | | | | | | | | | | | | | |
| 166 | ➔ | WALL 8 | 2 days | Sat 9/24/22 | Mon 9/26/22 | | | | | | | | | | | | | | | | | |
| 167 | ➔ | WALL 9 FRONTAGE | 2 days | Tue 9/27/22 | Wed 9/28/22 | | | | | | | | | | | | | | | | | |
| 168 | ➔ | ROAD A FRONT AND TRACK I | 30 days | Fri 10/28/22 | Tue 12/6/22 | | | | | | | | | | | | | | | | | |
| 169 | ➔ | Subgrade | 4 days | Fri 10/28/22 | Tue 11/1/22 | | | | | | | | | | | | | | | | | |
| 170 | ➔ | ROCK | 2 days | Wed 11/2/22 | Thu 11/3/22 | | | | | | | | | | | | | | | | | |
| 171 | ➔ | JUT CROSSING | 3 days | Thu 11/10/22 | Sat 11/12/22 | | | | | | | | | | | | | | | | | |
| 172 | ➔ | CURB POUR | 1 day | Fri 12/2/22 | Fri 12/2/22 | | | | | | | | | | | | | | | | | |
| 173 | ➔ | ROCK FOR ASPHALT | 2 days | Sat 12/3/22 | Mon 12/5/22 | | | | | | | | | | | | | | | | | |
| 174 | ➔ | ASPHALT PAVE | 1 day | Tue 12/6/22 | Tue 12/6/22 | | | | | | | | | | | | | | | | | |
| 175 | ➔ | ROAD B | 26 days | Wed 11/2/22 | Tue 12/6/22 | | | | | | | | | | | | | | | | | |
| 176 | ➔ | Subgrade | 2 days | Wed 11/2/22 | Thu 11/3/22 | | | | | | | | | | | | | | | | | |
| 177 | ➔ | ROCK | 2 days | Fri 11/4/22 | Mon 11/7/22 | | | | | | | | | | | | | | | | | |
| 178 | ➔ | JUT CROSSING | 4 days | Mon 11/14/22 | Thu 11/17/22 | | | | | | | | | | | | | | | | | |
| 179 | ➔ | CURB POUR | 1 day | Fri 12/2/22 | Fri 12/2/22 | | | | | | | | | | | | | | | | | |
| 180 | ➔ | ROCK FOR ASPHALT | 2 days | Sat 12/3/22 | Mon 12/5/22 | | | | | | | | | | | | | | | | | |

Project: Tolt Schedule Utility Re
Date: Fri 11/4/22


| | | | | | | | | | |
|-----------|--|--------------------|--|-----------------------|--|--------------------|--|-----------------|--|
| Task | | Project Summary | | Manual Task | | Start-only | | Deadline | |
| Split | | Inactive Task | | Duration-only | | Finish-only | | Progress | |
| Milestone | | Inactive Milestone | | Manual Summary Rollup | | External Tasks | | Manual Progress | |
| Summary | | Inactive Summary | | Manual Summary | | External Milestone | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Qtr 2, 2022 | | | Qtr 3, 2022 | | | Qtr 4, 2022 | | | Qtr 1, 2023 | | Qtr 2, 2023 | | Qtr 3, 2023 | |
|-----|-----------|------------------------------|----------------|--------------------|--------------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-------------|-----|-------------|-----|
| | | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun |
| 181 | → | ASPHALT | 1 day | Tue 12/6/22 | Tue 12/6/22 | | | | | | | | | | | | | | | |
| 182 | → | ROAD C | 24 days | Fri 11/4/22 | Tue 12/6/22 | | | | | | | | | | | | | | | |
| 183 | → | SUBGRADE | 1 day | Fri 11/4/22 | Fri 11/4/22 | | | | | | | | | | | | | | | |
| 184 | → | ROCK | 2 days | Mon 11/7/22 | Tue 11/8/22 | | | | | | | | | | | | | | | |
| 185 | → | JUT CROSSING | 4 days | Fri 11/18/22 | Tue 11/22/22 | | | | | | | | | | | | | | | |
| 186 | → | CURB POUR | 1 day | Thu 12/1/22 | Thu 12/1/22 | | | | | | | | | | | | | | | |
| 187 | → | ROCK FOR ASPHALT | 2 days | Fri 12/2/22 | Sat 12/3/22 | | | | | | | | | | | | | | | |
| 188 | → | ASPHAT | 2 days | Mon 12/5/22 | Tue 12/6/22 | | | | | | | | | | | | | | | |
| 189 | → | ROAD D | 22 days | Mon 11/7/22 | Mon 12/5/22 | | | | | | | | | | | | | | | |
| 190 | → | SUBGRADE | 1 day | Mon 11/7/22 | Mon 11/7/22 | | | | | | | | | | | | | | | |
| 191 | → | ROCK | 2 days | Tue 11/8/22 | Wed 11/9/22 | | | | | | | | | | | | | | | |
| 192 | → | JUT CROSSING | 4 days | Wed 11/23/22 | Wed 11/30/22 | | | | | | | | | | | | | | | |
| 193 | → | CURB POUR | 1 day | Thu 12/1/22 | Thu 12/1/22 | | | | | | | | | | | | | | | |
| 194 | → | ROCK FOR ASPHALT | 2 days | Fri 12/2/22 | Sat 12/3/22 | | | | | | | | | | | | | | | |
| 195 | → | ASPHALT | 1 day | Mon 12/5/22 | Mon 12/5/22 | | | | | | | | | | | | | | | |
| 196 | → | TRACT F | 21 days | Tue 11/8/22 | Mon 12/5/22 | | | | | | | | | | | | | | | |
| 197 | → | SUBGRADE | 1 day | Tue 11/8/22 | Tue 11/8/22 | | | | | | | | | | | | | | | |
| 198 | → | ROCK | 1 day | Wed 11/9/22 | Wed 11/9/22 | | | | | | | | | | | | | | | |
| 199 | → | CURB POUR | 1 day | Fri 12/2/22 | Fri 12/2/22 | | | | | | | | | | | | | | | |
| 200 | → | ROCK FOR ASPHALT | 1 day | Sat 12/3/22 | Sat 12/3/22 | | | | | | | | | | | | | | | |
| 201 | → | ASPHALT | 1 day | Mon 12/5/22 | Mon 12/5/22 | | | | | | | | | | | | | | | |
| 202 | → | IMPORT DIRT | 30 days | Tue 8/9/22 | Tue 9/13/22 | | | | | | | | | | | | | | | |
| 203 | → | TRACT M POND | 10 days | Wed 9/14/22 | Sat 9/24/22 | | | | | | | | | | | | | | | |
| 204 | → | JUT | 30 days | Wed 12/7/22 | Thu 1/12/23 | | | | | | | | | | | | | | | |
| 205 | → | WEST JUST EX | 8 days | Wed 12/7/22 | Thu 12/15/22 | | | | | | | | | | | | | | | |
| 206 | → | Install JUT | 15 days | Fri 12/16/22 | Wed 1/4/23 | | | | | | | | | | | | | | | |
| 207 | → | BACKFILL JUT | 7 days | Thu 1/5/23 | Thu 1/12/23 | | | | | | | | | | | | | | | |
| 208 | → | SIDEWALKS | 16 days | Fri 1/13/23 | Wed 2/1/23 | | | | | | | | | | | | | | | |
| 209 | → | WEST SIDEWALKS AND DRIVEWAYS | 16 days | Fri 1/13/23 | Wed 2/1/23 | | | | | | | | | | | | | | | |
| 210 | → | EAST JUST | 4 days | Sat 2/25/23 | Wed 3/1/23 | | | | | | | | | | | | | | | |
| 211 | → | JUT CROSSING | 4 days | Sat 2/25/23 | Wed 3/1/23 | | | | | | | | | | | | | | | |
| 212 | → | EAST ROADAYS | 28 days | Thu 3/2/23 | Mon 4/3/23 | | | | | | | | | | | | | | | |
| 213 | → | ROAD SUBGRADE | 2 days | Thu 3/2/23 | Fri 3/3/23 | | | | | | | | | | | | | | | |
| 214 | → | CURB ROADS | 9 days | Sat 3/4/23 | Tue 3/14/23 | | | | | | | | | | | | | | | |
| 215 | → | POUR CURBS | 2 days | Wed 3/15/23 | Thu 3/16/23 | | | | | | | | | | | | | | | |
| 216 | → | TRACT CURBS | 6 days | Fri 3/17/23 | Thu 3/23/23 | | | | | | | | | | | | | | | |
| 217 | → | ROCK EAST ROADS | 7 days | Fri 3/24/23 | Fri 3/31/23 | | | | | | | | | | | | | | | |
| 218 | → | PAVE EAST ROADS | 2 days | Sat 4/1/23 | Mon 4/3/23 | | | | | | | | | | | | | | | |

Project: Tolt Schedule Utility Re
Date: Fri 11/4/22

| | | | | | | | | | |
|-----------|--|--------------------|--|-----------------------|--|--------------------|--|-----------------|--|
| Task | | Project Summary | | Manual Task | | Start-only | | Deadline | |
| Split | | Inactive Task | | Duration-only | | Finish-only | | Progress | |
| Milestone | | Inactive Milestone | | Manual Summary Rollup | | External Tasks | | Manual Progress | |
| Summary | | Inactive Summary | | Manual Summary | | External Milestone | | | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Qtr 2, 2022 | | | Qtr 3, 2022 | | | Qtr 4, 2022 | | | Qtr 1, 2023 | | | Qtr 2, 2023 | | | Qtr 3, 2023 | |
|-----|-----------|-------------------|----------------|-------------------|-------------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|--|
| | | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | |
| 219 | | JUT EAST | 30 days | Tue 4/4/23 | Mon 5/8/23 | | | | | | | | | | | | | | | | | |
| 220 | | JUT EX EAST | 8 days | Tue 4/4/23 | Wed 4/12/23 | | | | | | | | | | | | | | | | | |
| 221 | | INSTALL JUT EAST | 15 days | Thu 4/13/23 | Sat 4/29/23 | | | | | | | | | | | | | | | | | |
| 222 | | BACKFILL JUT EAST | 7 days | Mon 5/1/23 | Mon 5/8/23 | | | | | | | | | | | | | | | | | |
| 223 | | WALKS EAST | 21 days | Tue 5/9/23 | Thu 6/1/23 | | | | | | | | | | | | | | | | | |
| 224 | | SIDEWALKS EAST | 17 days | Tue 5/9/23 | Sat 5/27/23 | | | | | | | | | | | | | | | | | |
| 225 | | POUR WALKS EAST | 4 days | Mon 5/29/23 | Thu 6/1/23 | | | | | | | | | | | | | | | | | |

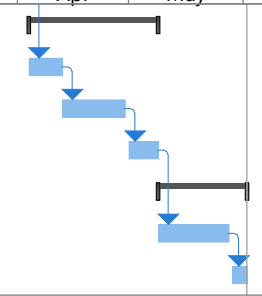

| | | | | | | | | | | |
|--|-----------|--|--------------------|--|-----------------------|--|--------------------|--|-----------------|--|
| Project: Tolt Schedule Utility Re Date: Fri 11/4/22 | Task | | Project Summary | | Manual Task | | Start-only | | Deadline | |
| | Split | | Inactive Task | | Duration-only | | Finish-only | | Progress | |
| | Milestone | | Inactive Milestone | | Manual Summary Rollup | | External Tasks | | Manual Progress | |
| | Summary | | Inactive Summary | | Manual Summary | | External Milestone | | | |
