

WIS 24 (W. FOREST HOME AVE) RESURFACING PROJECT

Project Location



WIS 24 (Forest Home Avenue) from just east of Janesville Road to 45th Street in Milwaukee County.

PROJECT UPDATE – September 5, 2025

Construction operations along WIS 24 (Forest Home Ave) continued this week between 68th Street and 43rd St and at the 76th St Bridge over Forest Home Ave.

Traffic:

WIS 24 lane closures are set along eastbound & westbound Forest Home Ave to define the work zone.
Traffic has been reduced to a single lane in each direction, with traffic being moved into the median lane.
Street parking along Forest Home Ave has been restricted within the work zone.
Access to properties (driveways and parking lots) will be maintained.

76th St bridge over Forest Home Ave: Traffic is in the median lanes with lane closures northbound & southbound on the outside

Contractor Operations this week:

Forest Home Ave (45th to Howard):

Continued installation of traffic signal bases at signalized intersections
Eastbound traffic was moved into the right-hand curb lane to accommodate work along the median (Howard to Oklahoma)

Forest Home Ave (Howard to 108th):

Continued placing concrete pavement in repair areas
Continued removals and concrete placement of curb & sidewalk
Continued interconnect conduit installation (boring) in medians 84th to 108th
Removed sections of beam guard for replacement
Began conduit installation for traffic signal loops
Began pavement joint repair

76th St:

Began removals of curb & sidewalk at the ramps to/from Forest Home

Next Week:

Forest Home Ave (45th to Howard):

Begin installation of conduit for street lighting (perpendicular runs)

Begin installation of lighting pull boxes

Forest Home Ave (Howard to 108th):

Continue sawcutting pavement for concrete repairs

Continue removals for curb & sidewalk replacement

Continue curb & sidewalk replacement

Continue interconnect conduit installation (boring) in medians 84th to 108th

Continue installation of conduit for traffic signal loops

Begin storm sewer inlet adjustments and repairs

76th St:

Begin concrete placement for curb & gutter / sidewalk at the ramps to Forest Home

Begin spot painting isolated corrosion on the steel girders of the bridge deck

WIS 24 (Forest Home Ave) - September 2nd thru 5th, 2025

Drilling dowel bars for a concrete pavement base patch



Placing concrete curb & gutter




Installing conduit for a traffic signal loops



Installing conduit in the median for traffic signal interconnect



Removing old beam guard for replacement

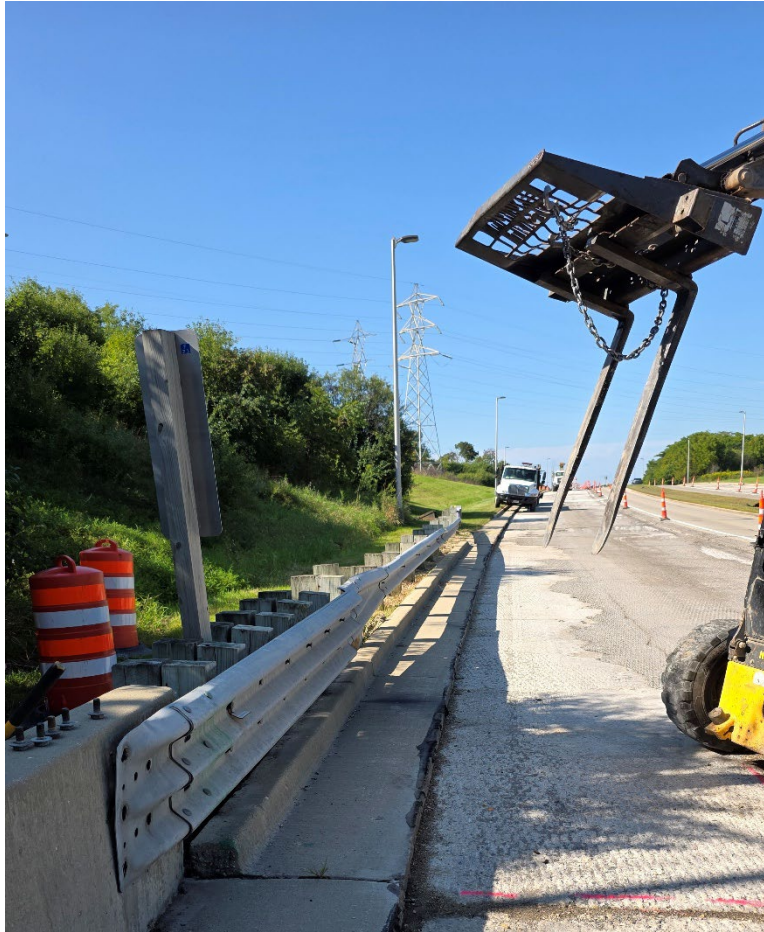

Cleaning pavement joints in preparation for repairs

