


















































ID		Task Mode	Task Name	Duration	Start	Finish	Task Calendar	Resource Names	r '13 W
1			<b>KFC Vietnam Order System</b>	<b>68 days</b>	<b>Fri 08/03/13</b>	<b>Tue 14/05/13</b>	<b>KFC</b>		
2			<b>Project initiation</b>	<b>13 days</b>	<b>Fri 08/03/13</b>	<b>Wed 20/03/13</b>	<b>KFC</b>		
3			Proposal	3 days	Fri 08/03/13	Sun 10/03/13	KFC	Hung	
4			Project plan	4 days	Mon 11/03/13	Thu 14/03/13	KFC	Hung	
5			Gathering requirement	6 days	Fri 15/03/13	Wed 20/03/13	KFC	Chuong,Han,Hoang	
6			<b>Planning</b>	<b>51 days</b>	<b>Thu 21/03/13</b>	<b>Fri 10/05/13</b>	<b>KFC</b>		
7			<b>Release 1 planning</b>	<b>31 days</b>	<b>Thu 21/03/13</b>	<b>Sat 20/04/13</b>	<b>KFC</b>		
8			Risk assessment	2 days	Thu 21/03/13	Fri 22/03/13	KFC	Hung	
9			<b>Story list</b>	<b>8 days</b>	<b>Thu 21/03/13</b>	<b>Thu 28/03/13</b>	<b>KFC</b>		
10			Client stories	3 days	Thu 21/03/13	Sat 23/03/13	KFC	Chuong,Tan,Han	
11			Stories priority	1 day	Sun 24/03/13	Sun 24/03/13	KFC	Chuong,Han,Hoang	
12			Stories estimate	1 day	Mon 25/03/13	Mon 25/03/13	KFC	Han,Tan	
13			Stories test	2 days	Tue 26/03/13	Wed 27/03/13	KFC	Hoang,Hung,Chuo	
14			Deliverable stories and document	1 day	Thu 28/03/13	Thu 28/03/13	KFC	Hung	
15			<b>Iteration and execution</b>	<b>23 days</b>	<b>Fri 29/03/13</b>	<b>Sat 20/04/13</b>	<b>KFC</b>		
16			Story list maintenance	1 day	Fri 29/03/13	Fri 29/03/13	KFC	Hung	
17			Breaking story	3 days	Sat 30/03/13	Mon 01/04/13	KFC	Chuong,Han	
18			Environment setup	1 day	Tue 02/04/13	Tue 02/04/13	KFC	Chuong,Han,Hoang	
19			Architectural design	2 days	Wed 03/04/13	Thu 04/04/13	KFC	Tan	
20			Database design	2 days	Fri 05/04/13	Sat 06/04/13	KFC	Chuong,Hung,Han	
21			Interface design	2 days	Sun 07/04/13	Mon 08/04/13	KFC	Chuong,Han	
22			Testcase	2 days	Tue 09/04/13	Wed 10/04/13	KFC	Chuong,Hoang	
23			Code	7 days	Thu 11/04/13	Wed 17/04/13	KFC	Han,Tan	
24			Unit test execution	2 days	Thu 18/04/13	Fri 19/04/13	KFC	Chuong,Hoang	

Project: Project Plan

Date: Mon 22/04/13

Task

Split


Milestone


Summary


Project Summary


Inactive Task


Inactive Milestone














Inactive Summary

Manual Task


Duration-only


Manual Summary Rollup


Manual Summary


Start-only


Finish-only


















External Tasks


External Milestone


Deadline


Progress


Manual Progress


























































ID		Task Mode	Task Name	Duration	Start	Finish	Task Calendar	Resource Names	
25			Release1 execution	1 day	Sat 20/04/13	Sat 20/04/13	KFC	Hung,Tan	
26			<b>Release 2 planning</b>	<b>20 days</b>	<b>Sun 21/04/13</b>	<b>Fri 10/05/13</b>	<b>KFC</b>		
27			Risk assessment	2 days	Sun 21/04/13	Mon 22/04/13	KFC	Hung	
28			<b>Story list</b>	<b>6 days</b>	<b>Sun 21/04/13</b>	<b>Fri 26/04/13</b>	<b>KFC</b>		
29			Adminstrator stories	2 days	Sun 21/04/13	Mon 22/04/13	KFC	Chuong,Han,Hoang	
30			Stories priority	1 day	Tue 23/04/13	Tue 23/04/13	KFC	Chuong,Han,Hoang	
31			Stories estimate	1 day	Wed 24/04/13	Wed 24/04/13	KFC	Han,Tan	
32			Stories test	1 day	Thu 25/04/13	Thu 25/04/13	KFC	Chuong,Hoang,Hung	
33			Deliverable stories and document	1 day	Fri 26/04/13	Fri 26/04/13	KFC	Hung	
34			<b>Iteration and execution</b>	<b>14 days</b>	<b>Sat 27/04/13</b>	<b>Fri 10/05/13</b>	<b>KFC</b>		
35			Story list maintenance	1 day	Sat 27/04/13	Sat 27/04/13	KFC	Chuong,Han,Hoang	
36			Breaking story	1 day	Sun 28/04/13	Sun 28/04/13	KFC	Han,Hung,Tan	
37			Architectural design	1 day	Mon 29/04/13	Mon 29/04/13	KFC	Han,Hung,Tan	
38			Database design	1 day	Tue 30/04/13	Tue 30/04/13	KFC	Han,Tan	
39			Interface design	1 day	Wed 01/05/13	Wed 01/05/13	KFC	Han,Hoang,Hung	
40			Testcase	2 days	Thu 02/05/13	Fri 03/05/13	KFC	Chuong,Hoang,Tan	
41			Code	4 days	Sat 04/05/13	Tue 07/05/13	KFC	Han,Tan	
42			Unit test execution	2 days	Wed 08/05/13	Thu 09/05/13	KFC	Chuong,Hoang,Hung	
43			Release2 execution	1 day	Fri 10/05/13	Fri 10/05/13	KFC	Hung	
44			<b>Implementation</b>	<b>4 days</b>	<b>Sat 11/05/13</b>	<b>Tue 14/05/13</b>	<b>KFC</b>		
45			User guider	1 day	Sat 11/05/13	Sat 11/05/13	KFC	Chuong,Han,Hoang	
46			Review all document	2 days	Sun 12/05/13	Mon 13/05/13	KFC	Chuong,Han,Hoang	
47			Deliver all document and product	1 day	Tue 14/05/13	Tue 14/05/13	KFC	Chuong,Han,Hoang	

Project: Project Plan

Date: Mon 22/04/13

Task

Split


Milestone


Summary


Project Summary


Inactive Task


Inactive Milestone














Inactive Summary

Manual Task


Duration-only


Manual Summary Rollup


Manual Summary


Start-only


Finish-only


















External Tasks


External Milestone


Deadline


Progress


Manual Progress













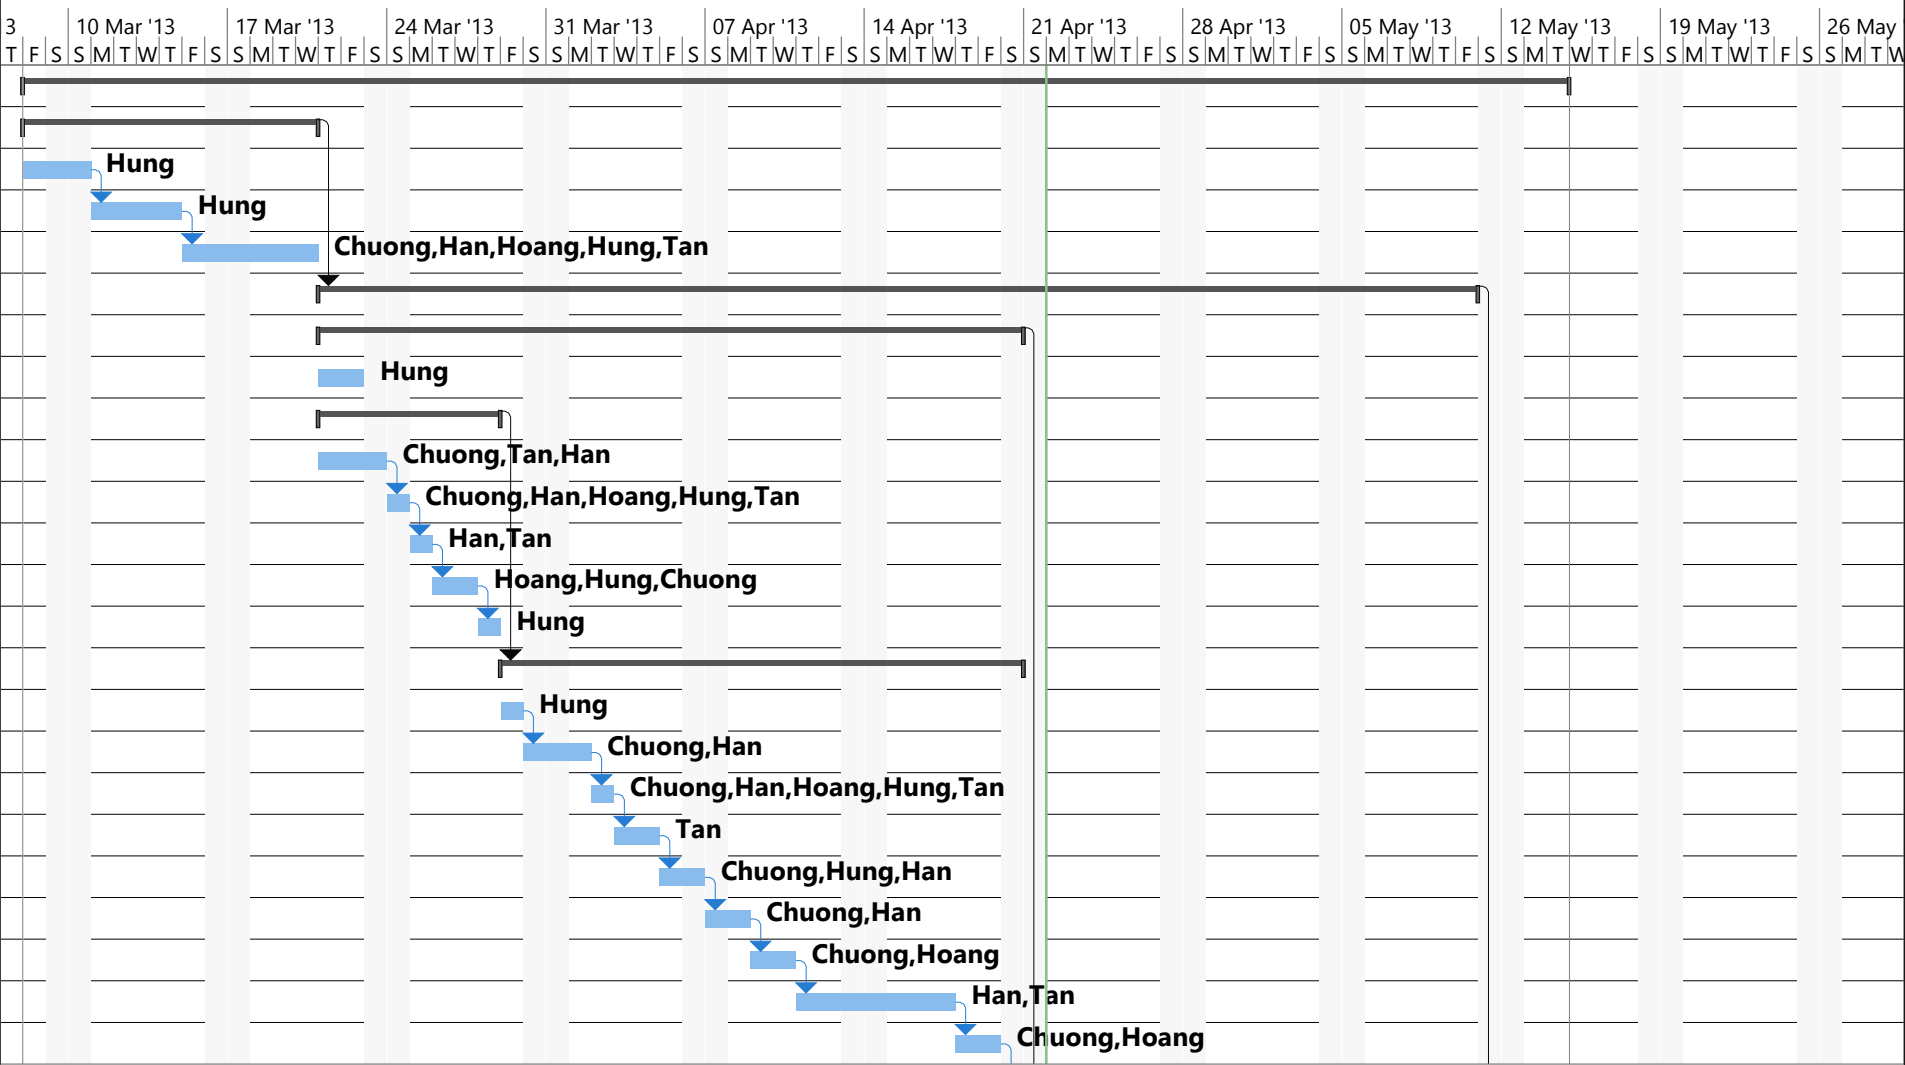

Project: Project Plan Date: Mon 22/04/13	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

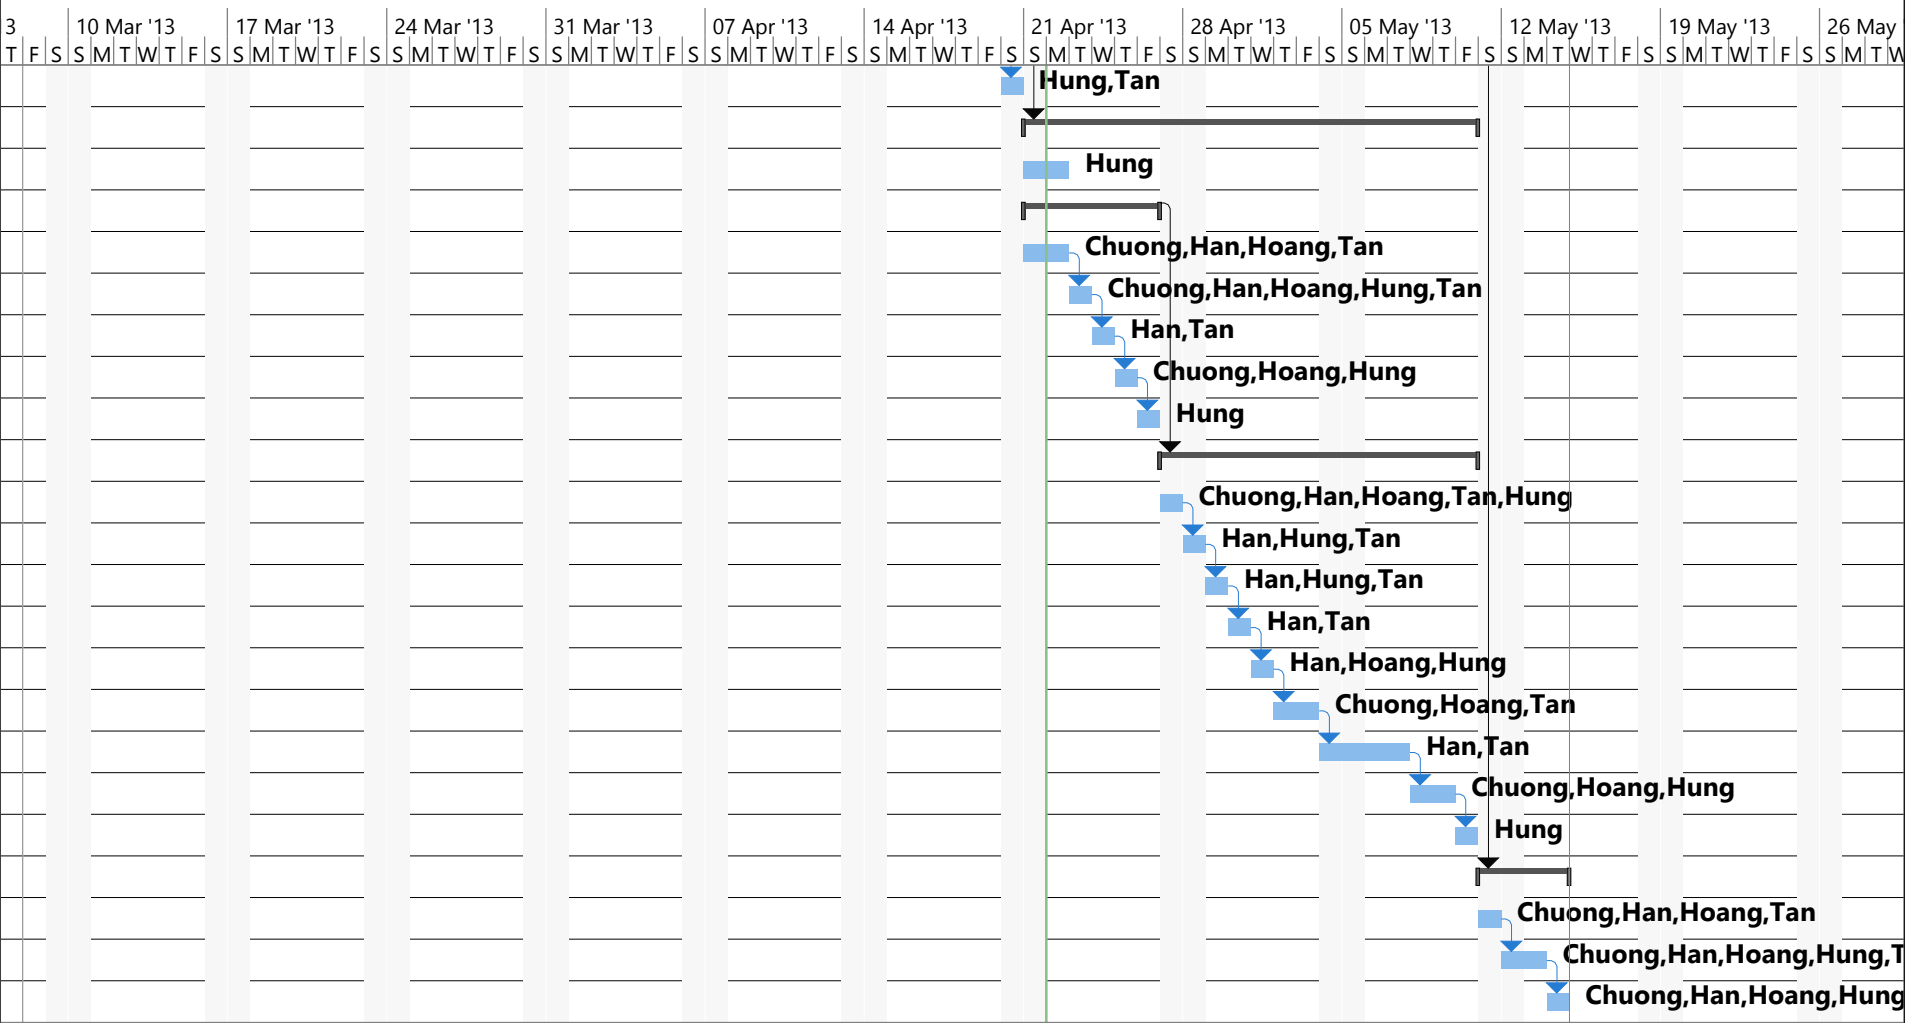

Project: Project Plan Date: Mon 22/04/13	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
