



# **Bristol Street Improvements Development/Construction Overview**

**April 2024**



---

Slide 1

---

Bristol Street Improvements  
Public Works Agency  
April 2024

# Completed Widening Projects

---

- St. Andrew Place to McFadden Avenue: Completed in 2002
- Elm Street to Memory Lane: Completed in 2002
- Pine Street to 3<sup>rd</sup> Street: Completed in 2010
- McFadden Avenue to Pine Street: Completed in 2011
- Bristol/Warner Intersection: Completed in 2012
- Bristol/17<sup>th</sup> Intersection: Completed in 2013
- 3<sup>rd</sup> Street to Civic Center Drive: Completed in 2014
- Washington Avenue to 17<sup>th</sup> Street: Completed in 2019



# Upcoming Bristol Projects


## Civic Center Drive to Washington Street

- Construction Schedule – 2<sup>nd</sup> Quarter 2024 to 4<sup>th</sup> Quarter 2025\*

## Warner Avenue to St. Andrew Place

- Construction Schedule – 4<sup>th</sup> Quarter 2024 to 2<sup>nd</sup> Quarter 2026\*

\*Schedule is dependent on South California Edison undergrounding coordination

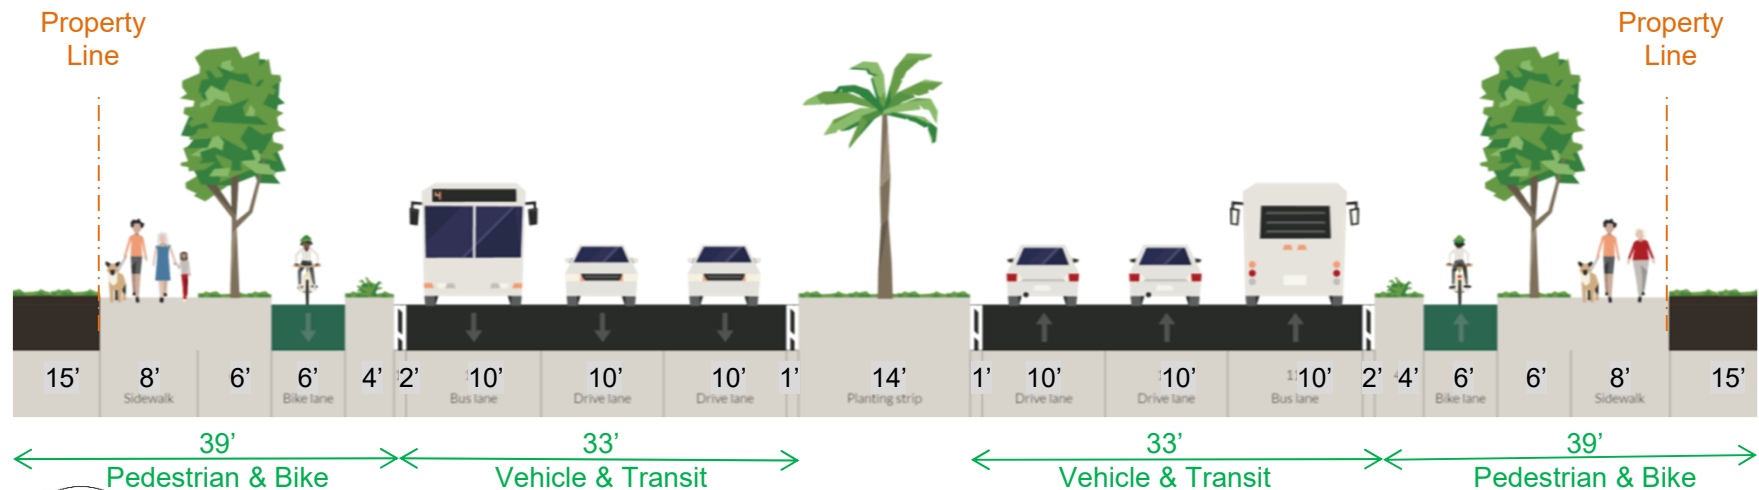

Slide 3

Bristol Street Improvements  
Public Works Agency  
April 2024

# Street Improvements

---

## Civic Center to Washington & Warner to St. Andrew

- Project includes one additional through lane and a buffered bike lane for both northbound and southbound traffic
- Infrastructure and safety improvements include new pavement, raised medians, raised buffers for bike lanes, traffic signal improvements, water improvements, and street lighting
- Aesthetic improvements include irrigation and landscaping enhancements in the raised medians and raised buffers as well as sound wall installation





# Bristol Utility Undergrounding

## Civic Center to Washington

- Utility undergrounding performed by utilities
- Trench #1: Telecommunication Companies
  - Crown Castle, Verizon, and Charter are current tenants on poles
  - Infrastructure will be relocated underground
  - Construction began the week of March 25<sup>th</sup>, contractor is HHS Construction
  - Construction Duration: 6-8 weeks of underground work (Mid May)  
2-3 weeks Cabling/Splicing (Beginning of June)
- Trench #2: Southern California Edison (SCE)
  - Power poles will be removed
  - Infrastructure will be relocated underground
  - Construction will follow telecommunication work
  - Currently, SCE permit is pending approval
  - SCE working will follow
- Community received notification from HHS Construction.



# What's Next?

---

## Civic Center to Washington

- Utility undergrounding started the week of March 25<sup>th</sup>.
- Construction for City's improvements anticipated for the 2<sup>nd</sup> Quarter of 2024.
- Work in TCE areas is beginning this month.
- Work will start following substantial completion of undergrounding work.
- Community will be notified when construction will begin.
- First items of work will be construction of sound walls.





**Thank you for your time!**



---

Slide 7

---

Bristol Street Improvements  
Public Works Agency  
April 2024

# Bristol Utility Undergrounding

---

## Warner to St. Andrew

- Utility undergrounding performed by City's contractor
- Single Trench: Southern California Edison (SCE) & Telecommunication Companies
  - Power poles will be removed
  - Crown Castle, Verizon, AT&T, Teleport Communications America, and Charter are current tenants on poles
  - Infrastructure will be relocated underground
- SCE and Telecommunication companies are working with City to finalize their plans. Plans are currently at 95%.
- Community will be notified when construction begins





# What's Next?

---

## Warner to St. Andrew

- Wrap up temporary construction easements and easement for utility relocation
- Utility undergrounding anticipated to start in late 2024 as part of the City's improvements by City's contractor
- Community will be notified when construction will begin
- First items of work will be construction of sound walls and work in TCE areas

