ID	Task Name	Duration	Start	Finish	Predecessors
1	**1. Survey and Documentation**	**157 days**	**Wed 5/10/23**	**Thu 12/14/23**	
8	**2. Design Options INT 2**	**122 days**	**Mon 7/10/23**	**Tue 12/26/23**	
11	**3. Interim 2 Addendum (Dewberry)**	**91 days**	**Tue 1/9/24**	**Tue 5/14/24**	
17	**4. Design Development**	**58 days**	**Wed 5/15/24**	**Fri 8/2/24**	
21	**4. 75 % Construction Documents**	**164 days**	**Mon 8/5/24**	**Thu 3/20/25**	
29	DSGN3060 DOB Submission	5 days	Mon 2/2/26	Fri 2/6/26	
30	**5. 100% Construction Documents**	**346 days**	**Fri 11/1/24**	**Fri 2/27/26**	
47	**6. Law Review**	**9 days**	**Fri 2/27/26**	**Wed 3/11/26**	
48	LAW1000 DDC Legal Review	9 days	Fri 2/27/26	Wed 3/11/26	46
49	**7. Procurement**	**194 days**	**Thu 3/12/26**	**Tue 12/8/26**	
50	ACCO2000 Procurement Summary	194 days	Thu 3/12/26	Tue 12/8/26	48
51	ACCO2010 Advertisement Period	35 days	Mon 3/30/26	Fri 5/15/26	48FS+12 days
52	ACCO2020 Execution/Contract Award	60 days	Mon 5/18/26	Fri 8/7/26	51
53	ACCO2030 Construction Contract Registration	35 days	Mon 8/10/26	Fri 9/25/26	52
54	**Pre-Construction**	**31 days**	**Wed 12/9/26**	**Wed 1/20/27**	
55	PCON1000 Contract Registration to NTP	31 days	Wed 12/9/26	Wed 1/20/27	50
56	**8. Construction**	**597 days**	**Wed 12/9/26**	**Thu 3/22/29**	
57	CONS0000 Site Safety Submit/Approval	75 days	Wed 12/9/26	Tue 3/23/27	50
58	CONS1000 Construction Contract Performance Period	566 days	Thu 1/21/27	Thu 3/22/29	55
59	CONS1010 Construction Kickoff Meeting	1 day	Thu 1/21/27	Thu 1/21/27	55
60	CONS1020 Pre-mobilization Submittals	45 days	Fri 1/22/27	Thu 3/25/27	59
61	CONS1030 Pull Permits	2 days	Fri 1/22/27	Mon 1/25/27	59
62	CONS1040 Contractor Mobilize to Site	7 days	Fri 3/26/27	Mon 4/5/27	60
63	CONS1050 Physical Construction	359 days	Tue 4/6/27	Fri 8/18/28	62
64	**9. Closeout**	**262 days**	**Mon 8/21/28**	**Tue 8/21/29**	
65	CLST1000 Project Closeout (365 CCDs)	262 days	Mon 8/21/28	Tue 8/21/29	63

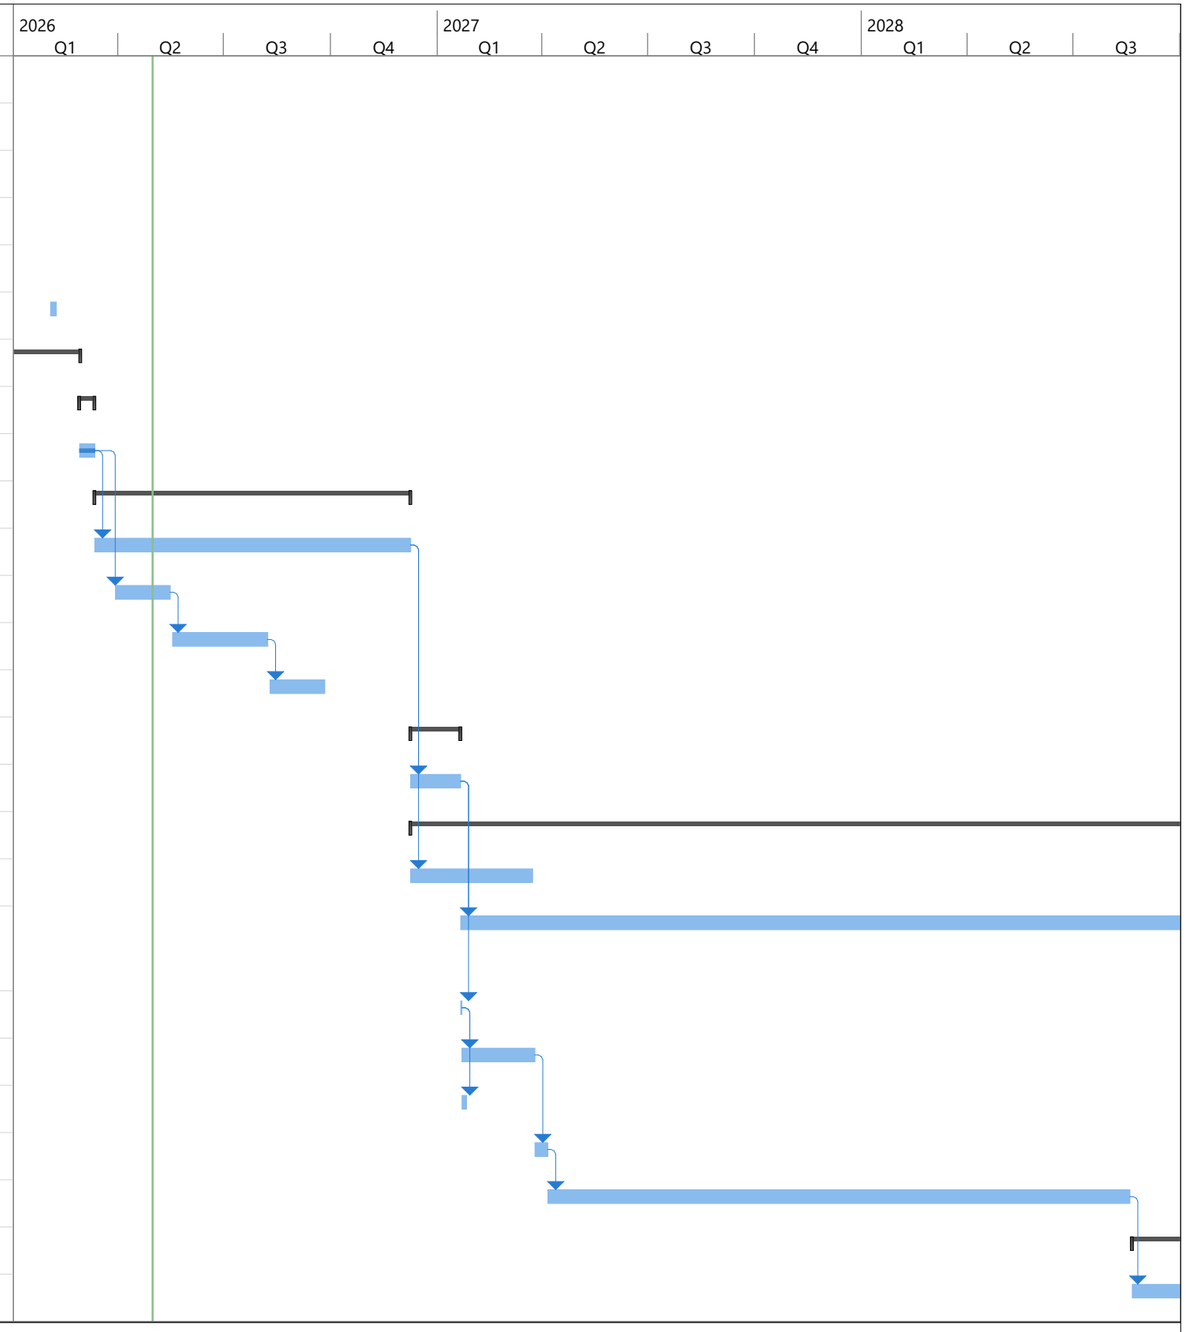

Project: PW77198CT - Bronx DA
Date: Fri 5/1/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone
